

## TRANSPORTATION POOLED FUND PROGRAM QUARTERLY PROGRESS REPORT

Lead Agency (University or Contractor):  Kansas DOT

**INSTRUCTIONS:**

*Project Managers and/or research project investigators should complete a quarterly progress report for each calendar quarter during which the projects are active. Please provide a project schedule status of the research activities tied to each task that is defined in the proposal; a percentage completion of each task; a concise discussion (2 or 3 sentences) of the current status, including accomplishments and problems encountered, if any. List all tasks, even if no work was done during this period.*

<b>Transportation Pooled Fund Project Number</b> TPF-5(351)	<b>Transportation Pooled Fund Program - Report Period:</b> <input type="checkbox"/> Quarter 1 (January 1 – March 31) <input type="checkbox"/> Quarter 2 (April 1 – June 30) <input type="checkbox"/> Quarter 3 (July 1 – September 30) <input checked="" type="checkbox"/> Quarter 4 (October 1 – December 31)	
<b>Project Title: Self De-icing LED Signals</b>		
<b>Project Manager:</b> Carla Anderson	<b>Phone:</b> 785-296-0357	<b>E-mail:</b> Carla.anderson@ks.gov
<b>Project Investigator:</b> Hongyi Cai	<b>Phone:</b> 785-864-2597	<b>E-mail:</b> hycai@ku.edu
<b>Lead Agency Project ID:</b> RE-0721-01	<b>Other Project ID (i.e., contract #):</b>	<b>Project Start Date:</b> August 15, 2016
<b>Original Project End Date:</b> August 2019	<b>Current Project End Date:</b> June 2021	<b>Number of Extensions:</b> 1

Project schedule status:

On schedule     
  On revised schedule     
  Ahead of schedule     
  Behind schedule

Overall Project Statistics:


Total Project Budget	Total Cost to Date for Project	Total Percentage of Work Completed
\$240,000 original, \$360,000 with addendum	\$325,488.63	90%

Quarterly Project Statistics:

Total Project Expenses This Quarter	Total Amount of Funds Expended This Quarter	Percentage of Work Completed This Quarter
\$13,584.06	\$13,584.06	3%

## Project Description:

This pooled fund project will develop and demonstrate new self-de-icing LED signals for highway signalized intersections and railroad signaling applications to solve a well-known problem of the existing LED signal light whose lens is too cool to melt snow and de-ice in wintery conditions. The self-de-icing LED signals will adopt one or both of two novel architectures (Figure 1), including (a) “Heated Lens Lighting Arrangement” that uses a single high-power LED and (b) “Heat Arrangement of LED Arrays in Low Profile” that deploys multiple LEDs. The heat generated by the LED(s) is harvested by the passive heat exchanger and stored to heat the lens for melting snow and de-icing in wintery conditions.

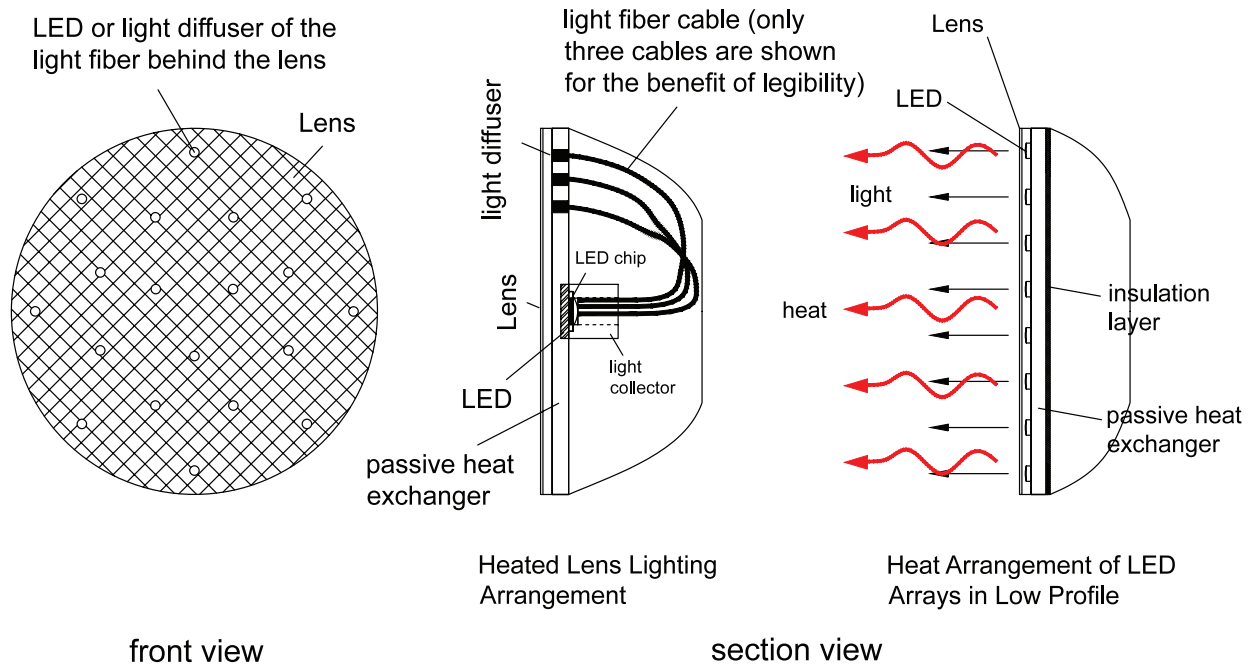

**Figure 1** The concept of the self-de-icing LED signal light, which adopts new architecture of “Heated Lens Lighting Arrangement” or “Heat Arrangement of LED Arrays in Low Profile”

Fully working prototypes of the self-de-icing LED signals have been developed and tested in the laboratory. They have been tested in closed-course settings on the roof of an engineering building followed by field tests on highway intersection or railroad wayside or at-grade crossing signal lights. Each participating agency is required to provide support of three years of funding (\$20,000/year, totaling \$60,000) and will be guaranteed a field test site in each state for testing the fully working prototypes catering to their specific needs of the new type of signals. The research team will work with each participating agency to identify the desired test site on highway intersections or rail track sections and the desired technical specifications for testing the prototypes.

The investigative approach for the proposed project is divided into three stages. Work in Stage 1 focuses on laboratory development and tests. Work in Stage 2 focuses on testing the three prototypes in a closed-course setting on the roof of the University of Kansas engineering complex and powered by the signal controller cabinet. Work in the third and final stage involves field testing of the developed prototypes on identified test sites. On-site demonstration of the prototype signals will also be held for project partners and state DOTs to initiate the implementation process. A final report will provide all relevant data and results along with plans for implementation of the self-de-icing LED signals in affected states.

**Progress this Quarter (includes meetings, work plan status, contract status, significant progress, etc.):**

During the fourth quarter (Oct 1, 2020 – Dec 31, 2020) of the project period, we have the following accomplishments.

In the present quarter (Oct 1, 2020 – Dec 31, 2020), first, the signal housing manufacturer has made 100 new samples of the finalized new self-de-icing signal housing, which have been finally delivered to our laboratory for testing and evaluation after a long time shipping by boat. The new housing samples were made using revised mass production technology by increasing the mold runner diameter size from 4 mm to 6 mm, which has corrected the defective concaved lens surface of the plastic housing in mass production, with a maximum tolerance of 1.5 mm. Meanwhile, the PC material of the new housing is Markrolon 2807 for UL certificate. All 100 new samples of the finalized housings have recently been tested with good performance.

Additionally, a new fresnel disc with 96 small fresnel lenses integrated on it has been designed with the desired improvements, and is currently being custom-made in a factory through injection mold. The new fresnel disc with 96 small fresnel lenses integrated on it will replace the old design of using separate 96 fresnel lenses. We are waiting for testing the 20 new samples of the new fresnel disc once they are made and shipped to our laboratory. The new fresnel disc with 96 small fresnel lenses integrated on is deemed a more cost-effective solution than using separate 96 fresnel lenses, and also as an alternative solution to the problem of uneven housing lens.

Furthermore, the field remote monitoring system with added mobile communication information device and data plan to remotely send signal performance data back to the laboratory on daily basis for real-time performance monitoring has been continuously tested on the roof for several months. We have installed the new remote monitoring system with mobile communication in the Lawrence test site, in addition to the original reliable “local” data monitoring system that kept running in the past year. All performance data were retrieved from the Lawrence test site showing the self-de-icing signals have been working properly. The self-de-icing signals have survived both winter and summer functioning as expected, without any signs of snow and ice accumulation on the signal lens in cold winter, and abnormal performance in hot summer. However, the newly added remote monitoring system with mobile communication mounted in Lawrence test site had records of network disconnection with unknown reasons and stopped sending data back to the laboratory. To solve the problem, we have been diagnosing the mobile system, also visited the Lawrence test site again for double checking the hardware. The problem might be related to an electronic part that is not reliable thus needs replacement. We are planning to schedule another visit to the test site to diagnose the hardware and try to solve this problem. Once the problem is solved, we will prepare the validated new remote monitoring system with mobile communication capability for uses in all test sites in other states.

Fifth generation of the prototypes of the final product are in preparation for other test sites. Seven states (Kansas, California, Michigan, New Jersey, Wisconsin, Pennsylvania, and Maryland) are participating in field testing and evaluation of the prototypes.

More details are listed as follows.

Firstly, we have tested the 100 new samples of the finalized new self-de-icing signal housing, which were made of Markrolon 2807 for UL certificate, using the revised mass production technology to correct the defective concaved lens surface of the plastic housing in mass production, with a maximum tolerance of 1.5 mm. The test results are summarized in Table 1. It was found that the average concaveness of the main signal housing lens is 1.24 mm with standard deviation of 0.64 mm, which is less than the maximum tolerance of 1.5 mm. Among the 100 samples, two samples are defective cannot be used, while the other two have tiny air bubbles that may not affect its use. Therefore, the new samples passed the quality inspection with a yield rate of 96%, meaning future products made with the revised mass production technology would have good quality with a maximum tolerance of the concaveness 1.5 mm. Figure 1 shows the pictures of the new samples.

Table 1: The measured depth of the concaveness of the main housing, which is the difference in height from the curve of the edge to the lens center, as well as inspection of the quality with other two parts of the housing.

Housing #	Center curved (mm)	Notes	Middle part	Back cover
1	2.5		ok	ok
2	2.5		ok	ok
3	0		ok	ok
4	1		ok	ok
5	0		ok	ok
6	1		ok	ok
7	1		ok	ok
8	defective	<b>misaligned screw</b>	ok	ok
9	1		ok	ok
10	2		ok	ok
11	2		ok	ok
12	2		ok	ok
13	1		ok	ok
14	1		ok	ok
15	1		ok	ok
16	1.5		ok	ok
17	1		ok	ok
18	1		ok	ok
19	1		ok	ok
20	defective	<b>cracks</b>	ok	ok
21	2		ok	ok
22	0		ok	ok
23	1		ok	ok
24	0		ok	ok
25	0		ok	ok
26	0		ok	ok
27	1		ok	ok
28	2		ok	ok
29	2		ok	ok
30	2		ok	ok
31	1		ok	ok
32	1		ok	ok
33	1		ok	ok
34	1.5	<b>tiny air bubble</b>	ok	ok
35	0.5		ok	ok
36	1		ok	ok
37	2		ok	ok
38	2		ok	ok
39	1.5		ok	ok
40	2		ok	ok
41	2		ok	ok
42	2		ok	ok
43	1.5		ok	ok
44	1		ok	ok
45	0		ok	ok
46	1		ok	ok
47	1		ok	ok
48	1.5		ok	ok
49	1		ok	ok
50	1.5		ok	ok

Housing #	Center curved (mm)	Notes	Middle part	Back cover
51	1		ok	ok
52	1		ok	ok
53	1.5		ok	ok
54	1		ok	ok
55	1		ok	ok
56	1	<b>tiny air bubble</b>	ok	ok
57	2		ok	ok
58	1.5		ok	ok
59	2		ok	ok
60	1.5		ok	ok
61	1		ok	ok
62	0		ok	ok
63	0.5		ok	ok
64	1.5		ok	ok
65	1.5		ok	ok
66	0		ok	ok
67	1		ok	ok
68	1.5		ok	ok
69	2		ok	ok
70	1		ok	ok
71	2		ok	ok
72	1.5		ok	ok
73	1		ok	ok
74	2		ok	ok
75	1		ok	ok
76	2		ok	ok
77	0		ok	ok
78	0		ok	ok
79	0		ok	ok
80	1		ok	ok
81	1		ok	ok
82	2		ok	ok
83	1		ok	ok
84	1		ok	ok
85	2		ok	ok
86	1		ok	ok
87	1		ok	ok
88	1		ok	ok
89	1		ok	ok
90	1.5		ok	ok
91	2		ok	ok
92	1.5		ok	ok
93	1.5		ok	ok
94	1.5		ok	ok
95	2		ok	ok
96	1		ok	ok
97	2		ok	ok
98	1.5		ok	ok
99	2		ok	ok
100	1.5		ok	ok




**Figure 1** New samples of the finalized new self-de-icing signal housing, made of PC material Markrolon 2807 for UL certificate using revised mass production technology to correct the defective concaved lens surface of the plastic housing in mass production, with a maximum tolerance of 1.5 mm.

Secondly, we have improved the design of the new fresnel disc with 96 small fresnel lenses integrated on it, as shown in Figure 2. Improvements include (1) four stiffeners are now added on the back to support the large disc to make it even on the front surface, (2) enlarged the four installation holes from diameter 8 mm to diameter 12.1 mm, (3) slightly decreased the disc diameter from 261 mm to 260 mm. The new lens disc has requirements on materials as UV stabilized clear PC materials with light transmittance of 85% - 90%, and



stable temperature from  $-30^{\circ}\text{C}$  ( $-22^{\circ}\text{F}$ ) to  $+120^{\circ}\text{C}$  ( $+248^{\circ}\text{F}$ ), ideally with some UL94 rating for fire resistance. A good choice is Markrolon 2807 or similar. The new fresnel lens disc is currently being custom-made in a factory using injection mold.

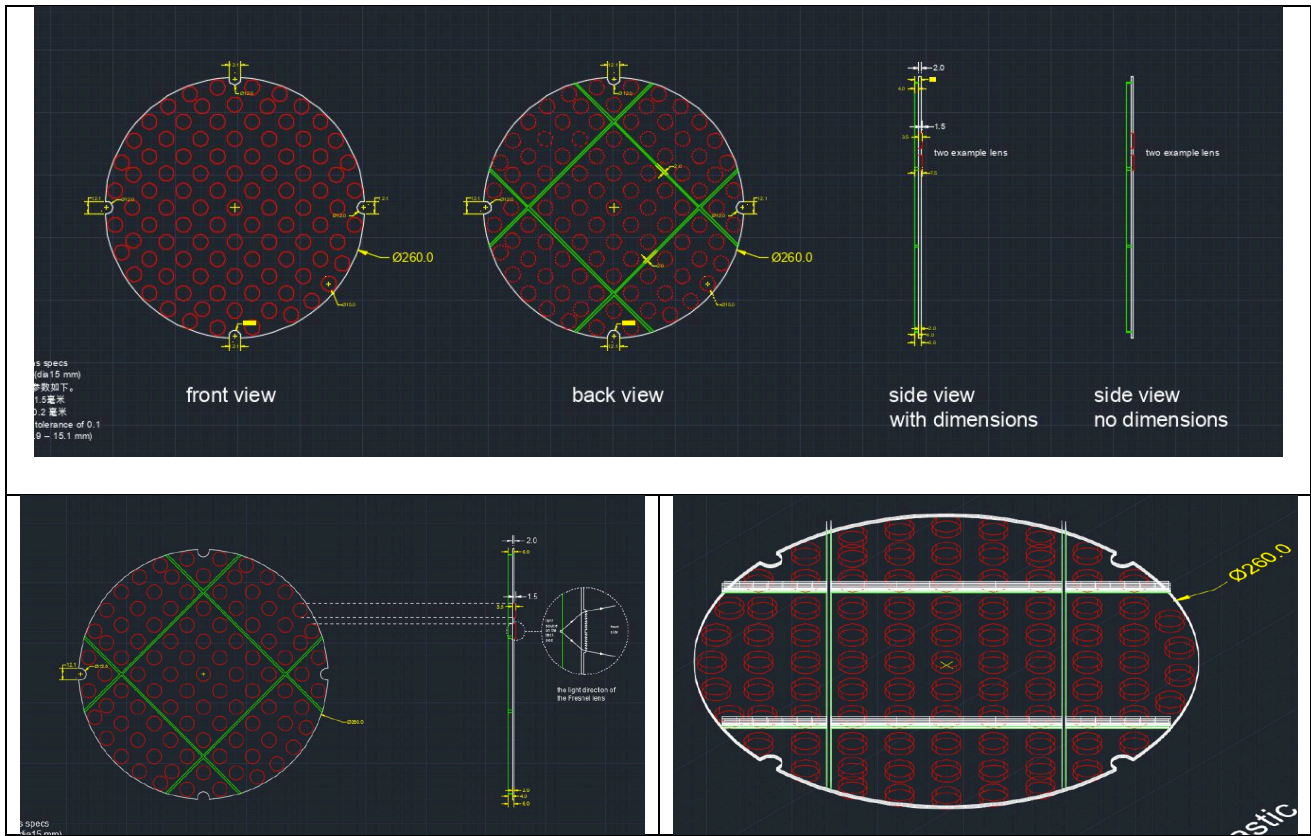


**Figure 2** Improved design of the new fresnel disc with 96 small fresnel lenses integrated on it

Furthermore, as shown in Figure 3, we have installed the new remote monitoring system with mobile communication in the Lawrence test site, in addition to the original reliable “local” data monitoring system that kept running in the past year. All performance data were retrieved from the Lawrence test site showing the self-de-icing signals have been working properly. The self-de-icing signals have survived both winter and summer functioning as expected, without any signs of snow and ice accumulation on the signal lens in cold winter, and abnormal performance in hot summer, as shown in Figure 4 on the hottest days and coldest days. Figure 5 shows some example pictures of the signals taken continuously at different time on different dates.




**Figure 3** Improved design of the new fresnel disc with 96 small fresnel lenses integrated on it

### 12\_18\_2019

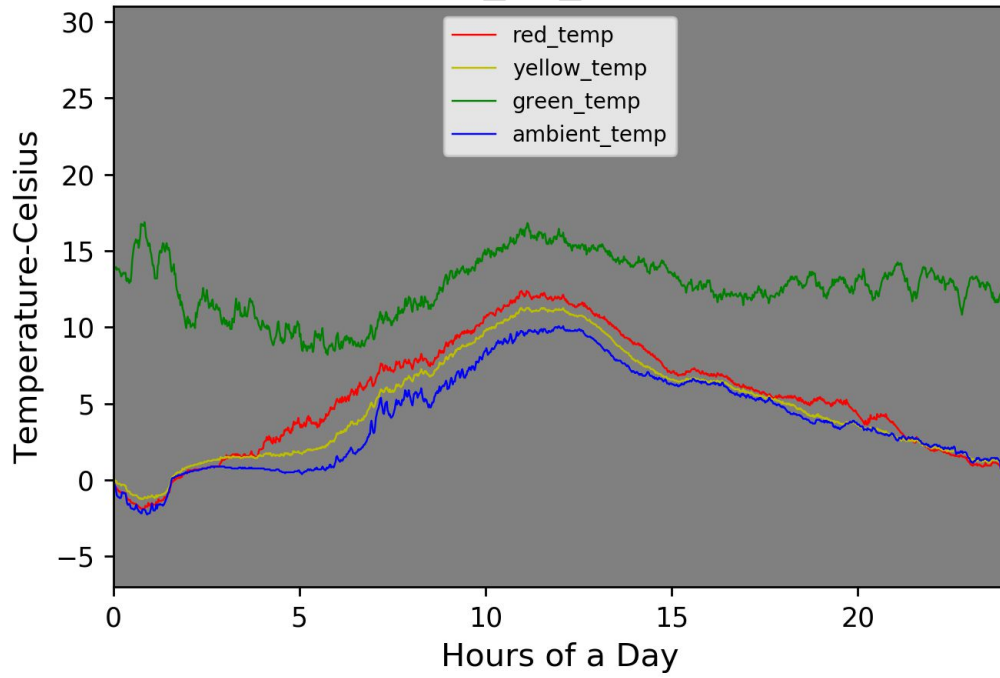


### 12\_31\_2019

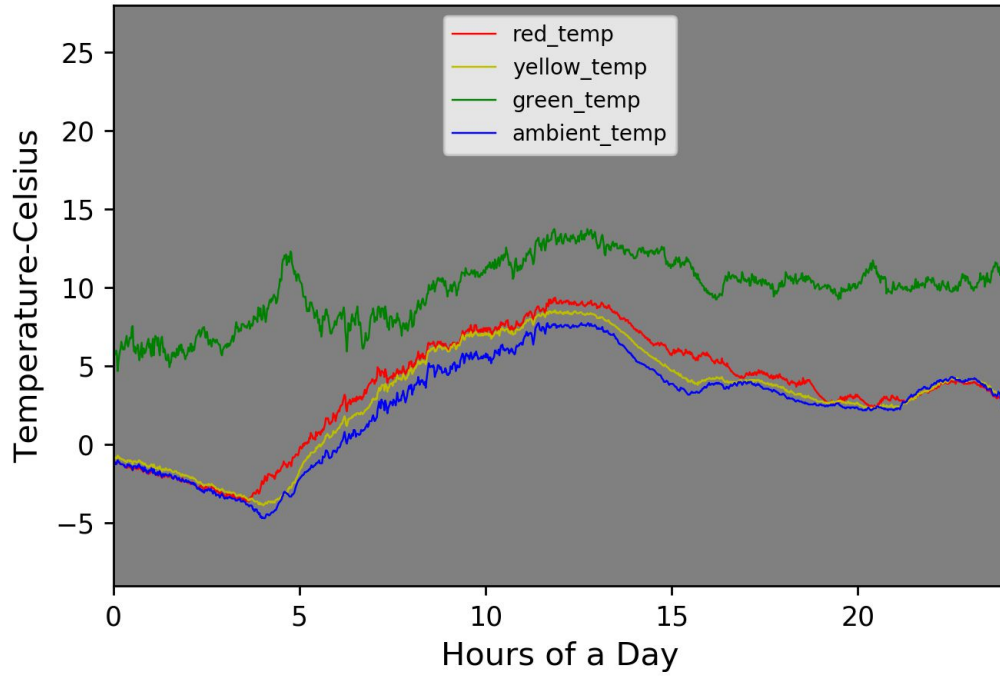





01\_06\_2020

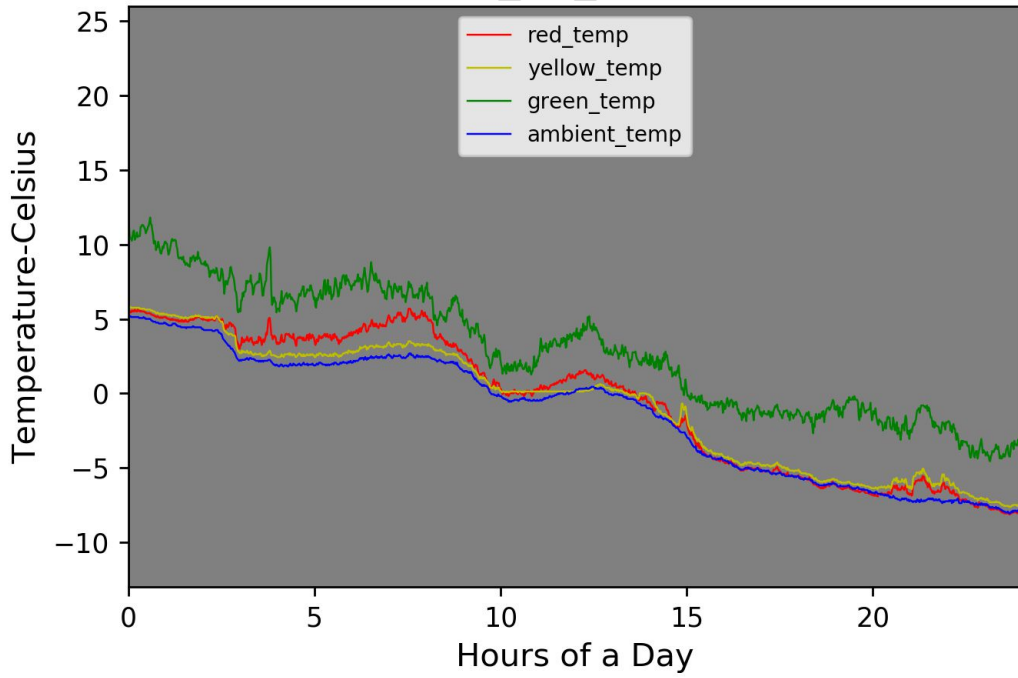


01\_08\_2020

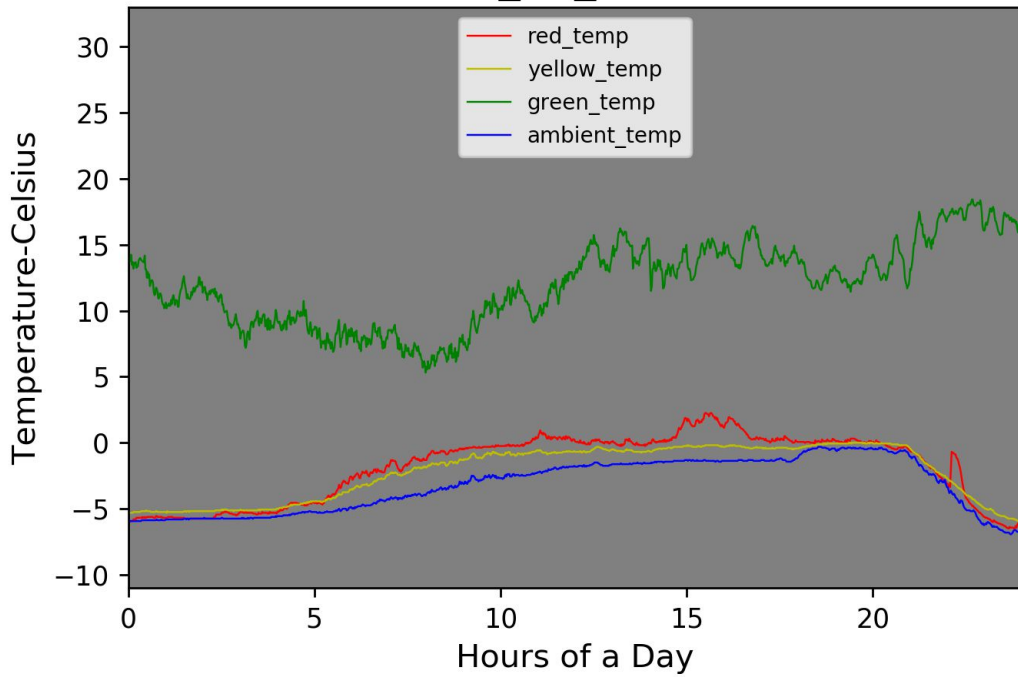


01\_16\_2020

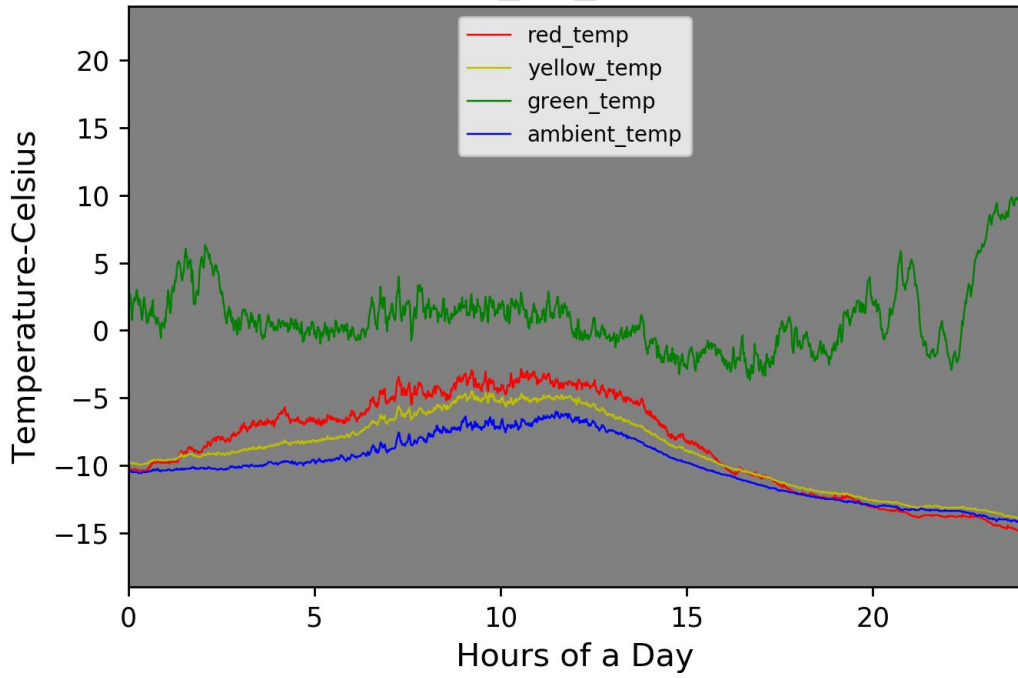


02\_09\_2020

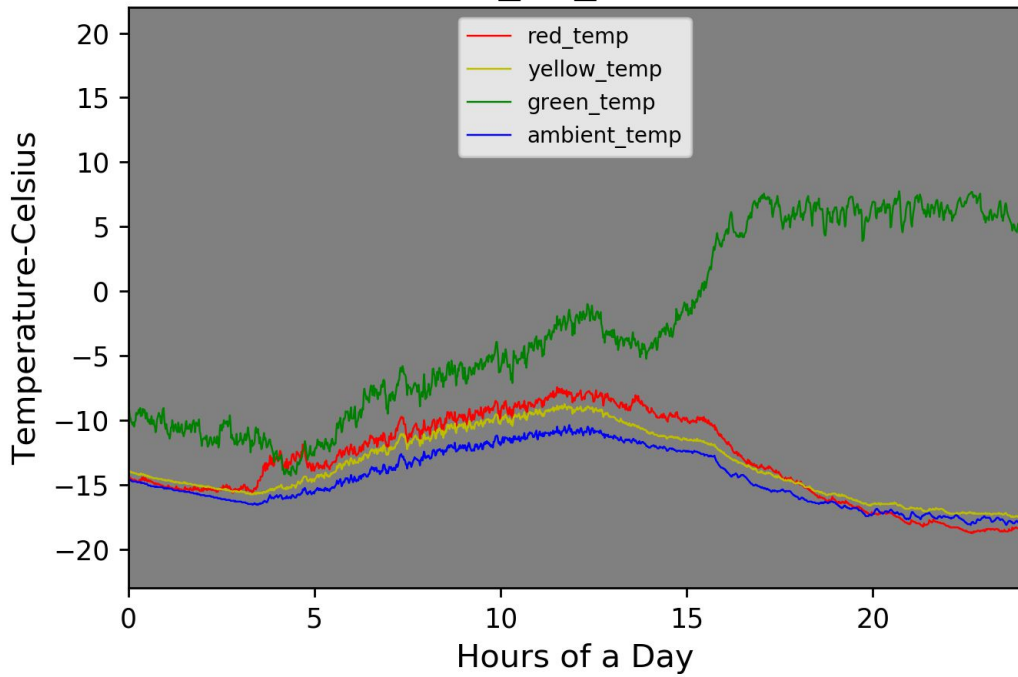


02\_10\_2020

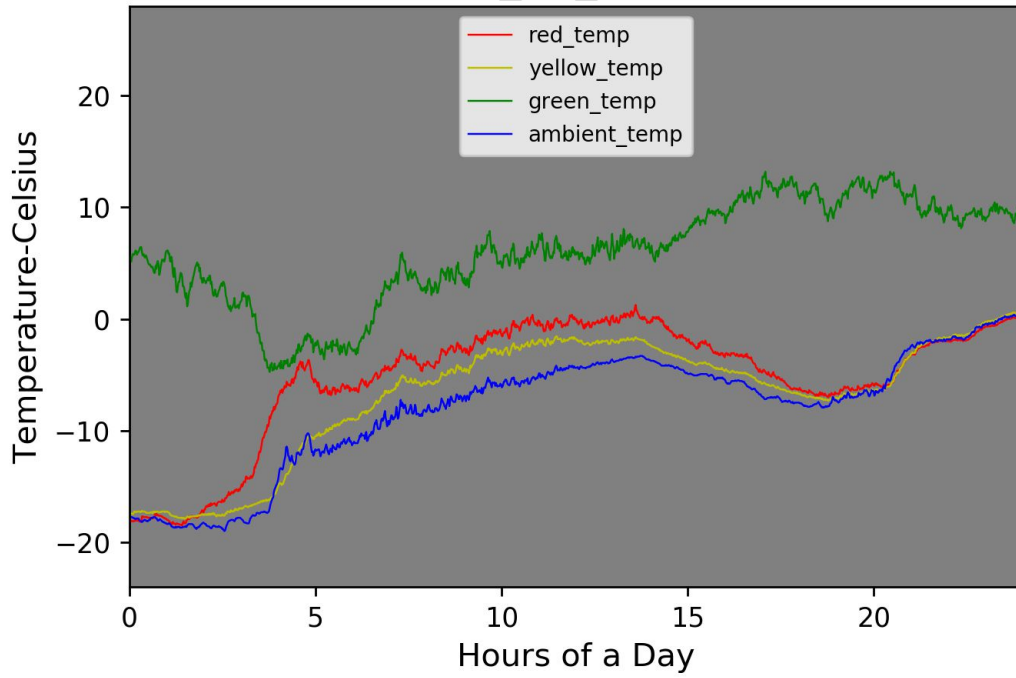


02\_17\_2020

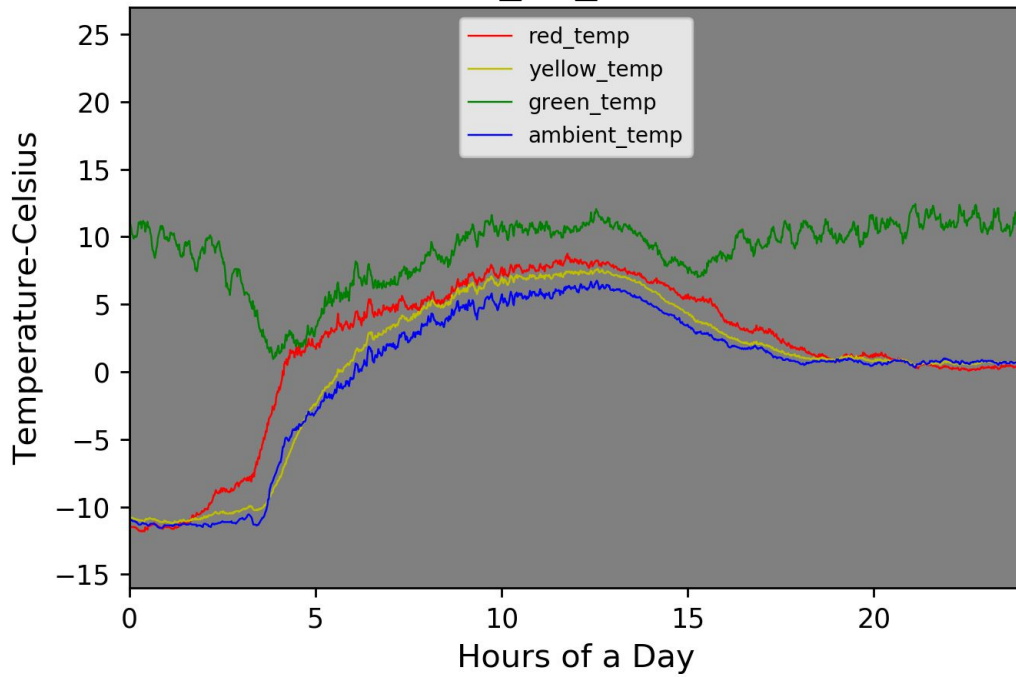


07\_07\_2020

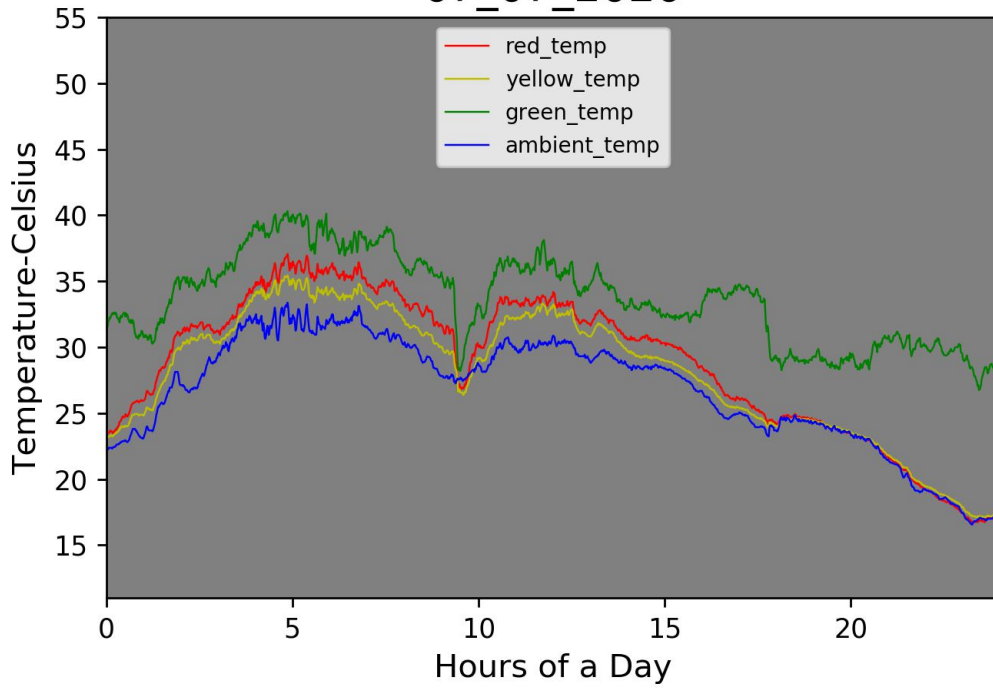


07\_18\_2020

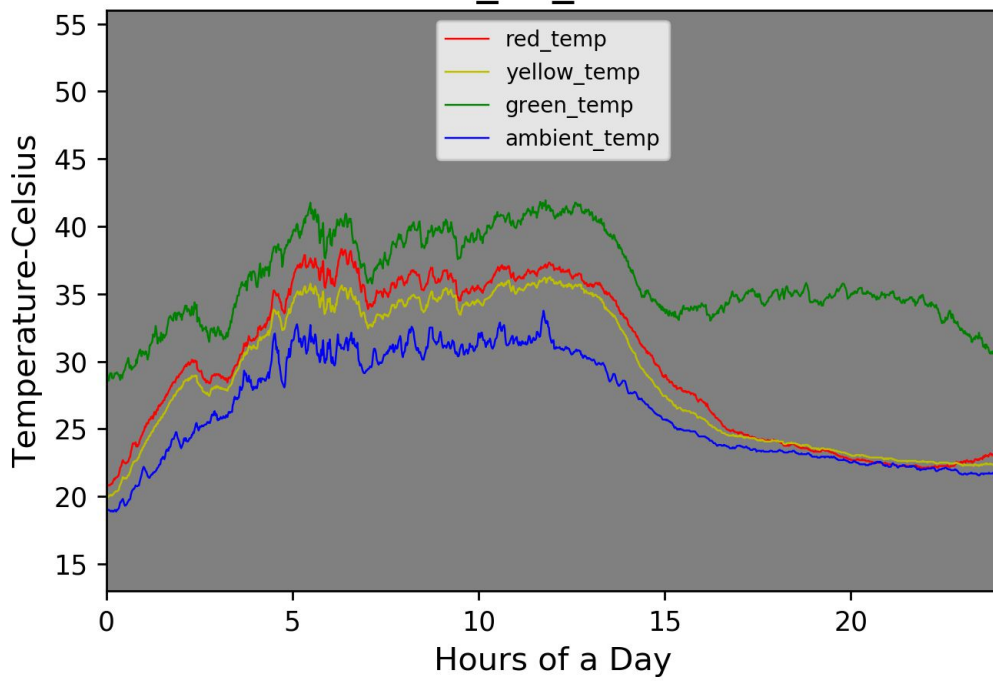

07\_24\_2020

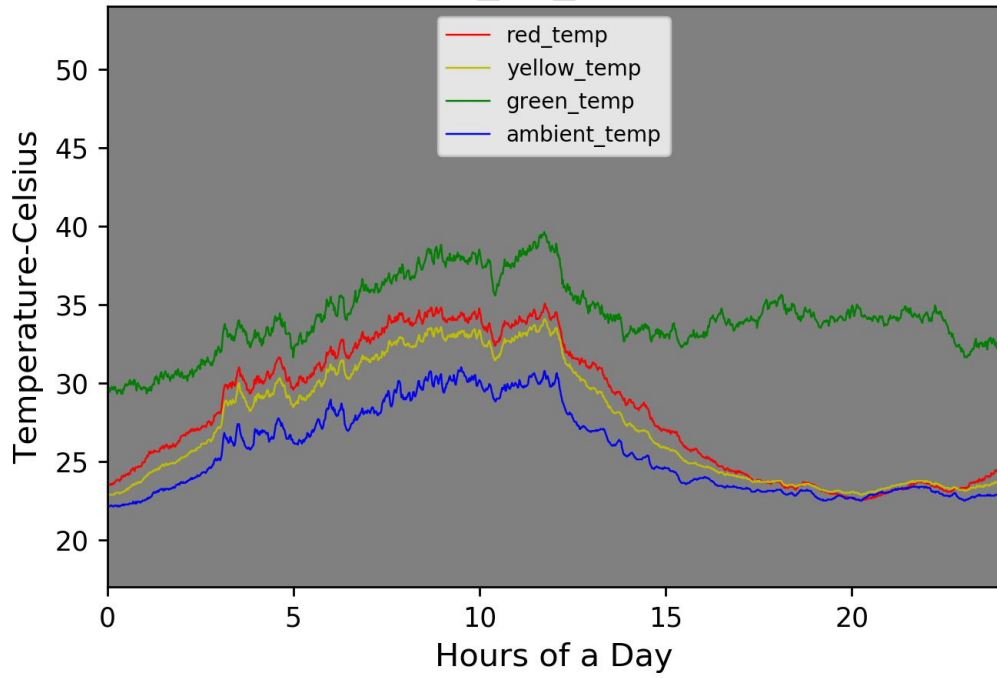


08\_08\_2020

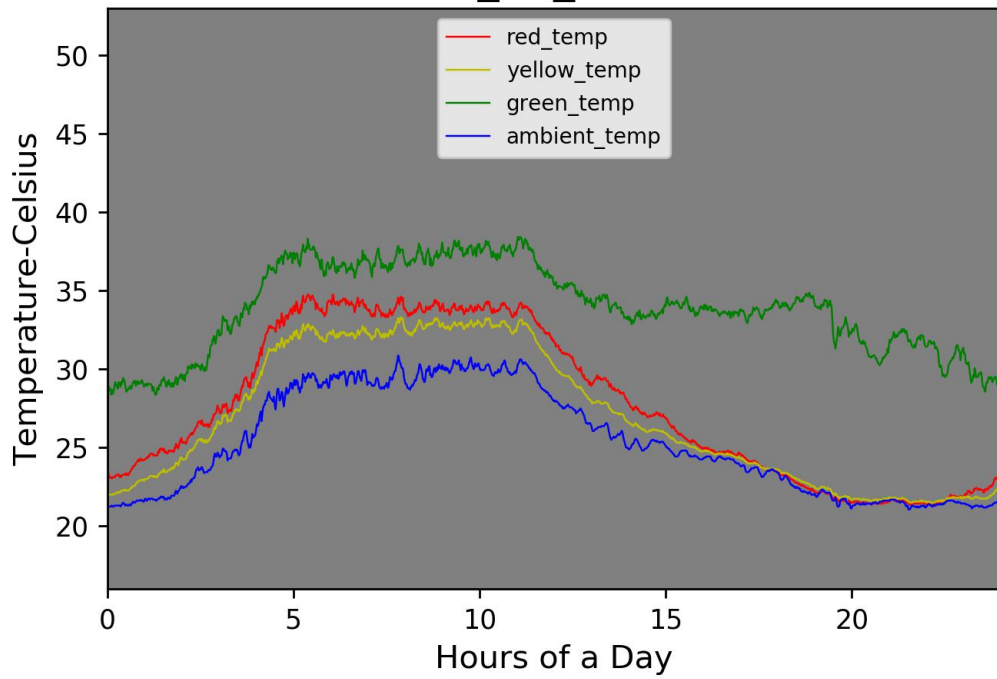






08\_17\_2020

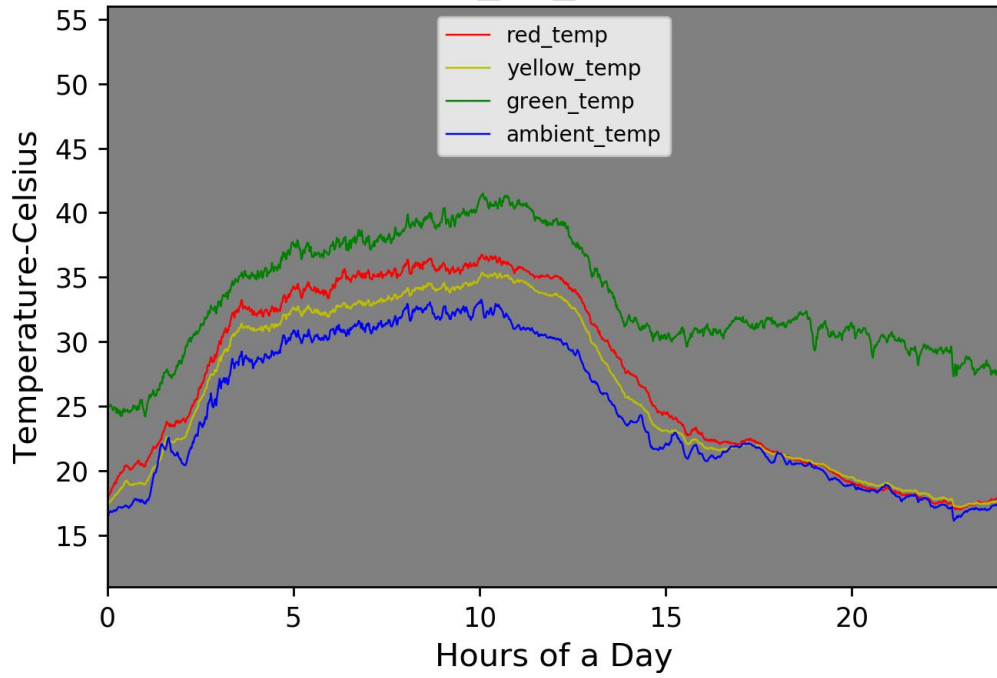


08\_24\_2020

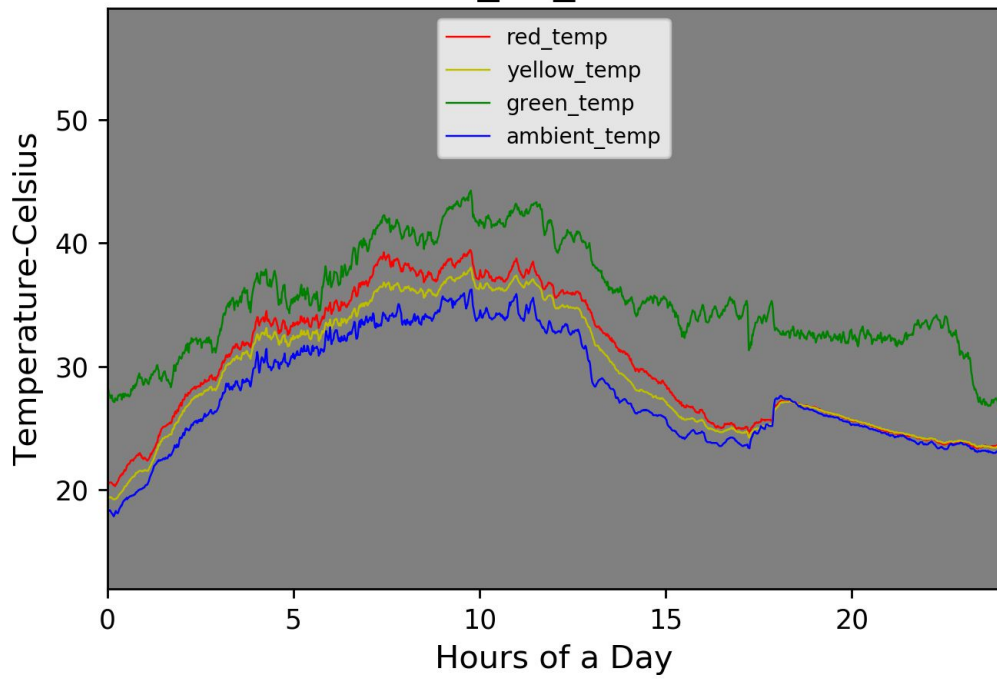

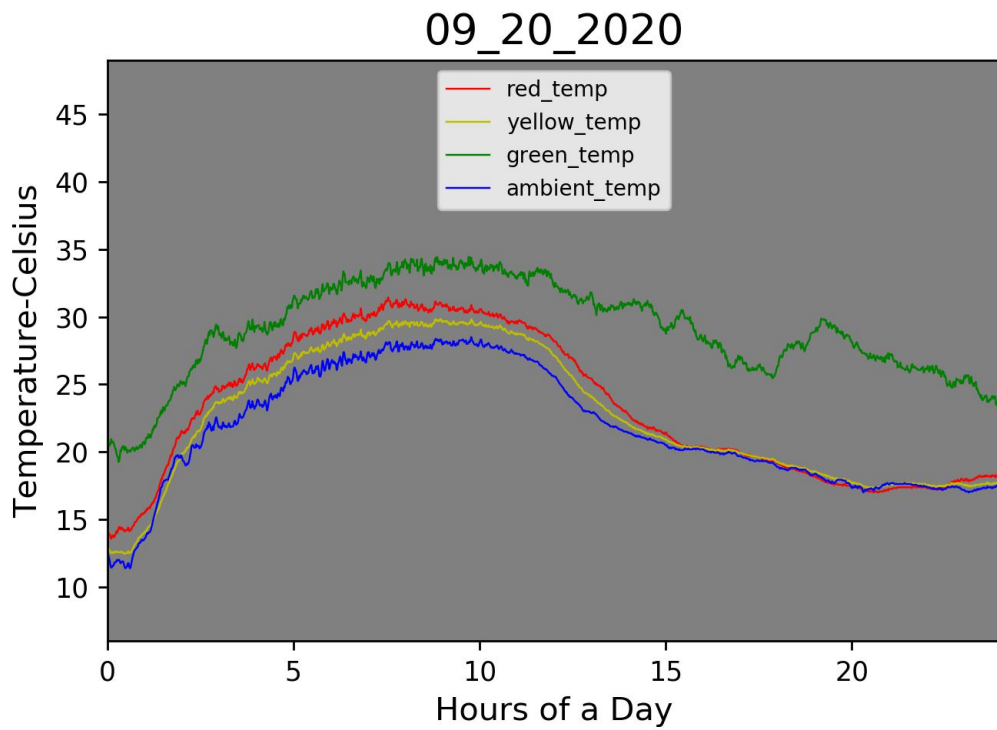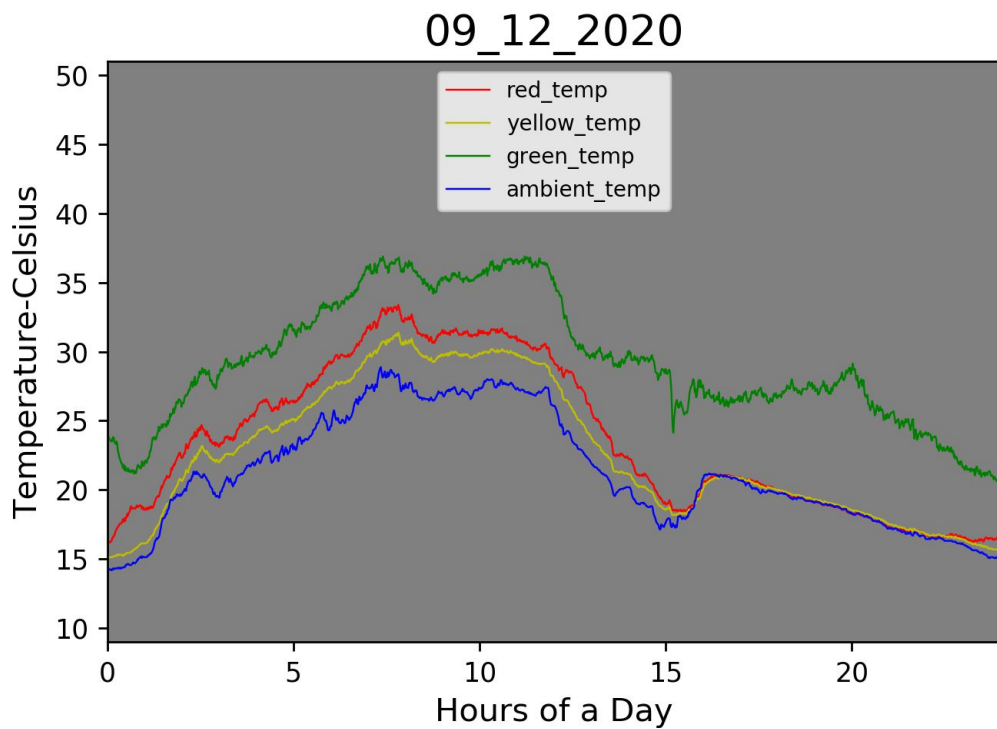

**Figure 4** Lawrence field test data during the hottest days in summer 2020 and winter 2019-2020, showing the performance of the red, yellow, and green signal lights under different weather conditions.

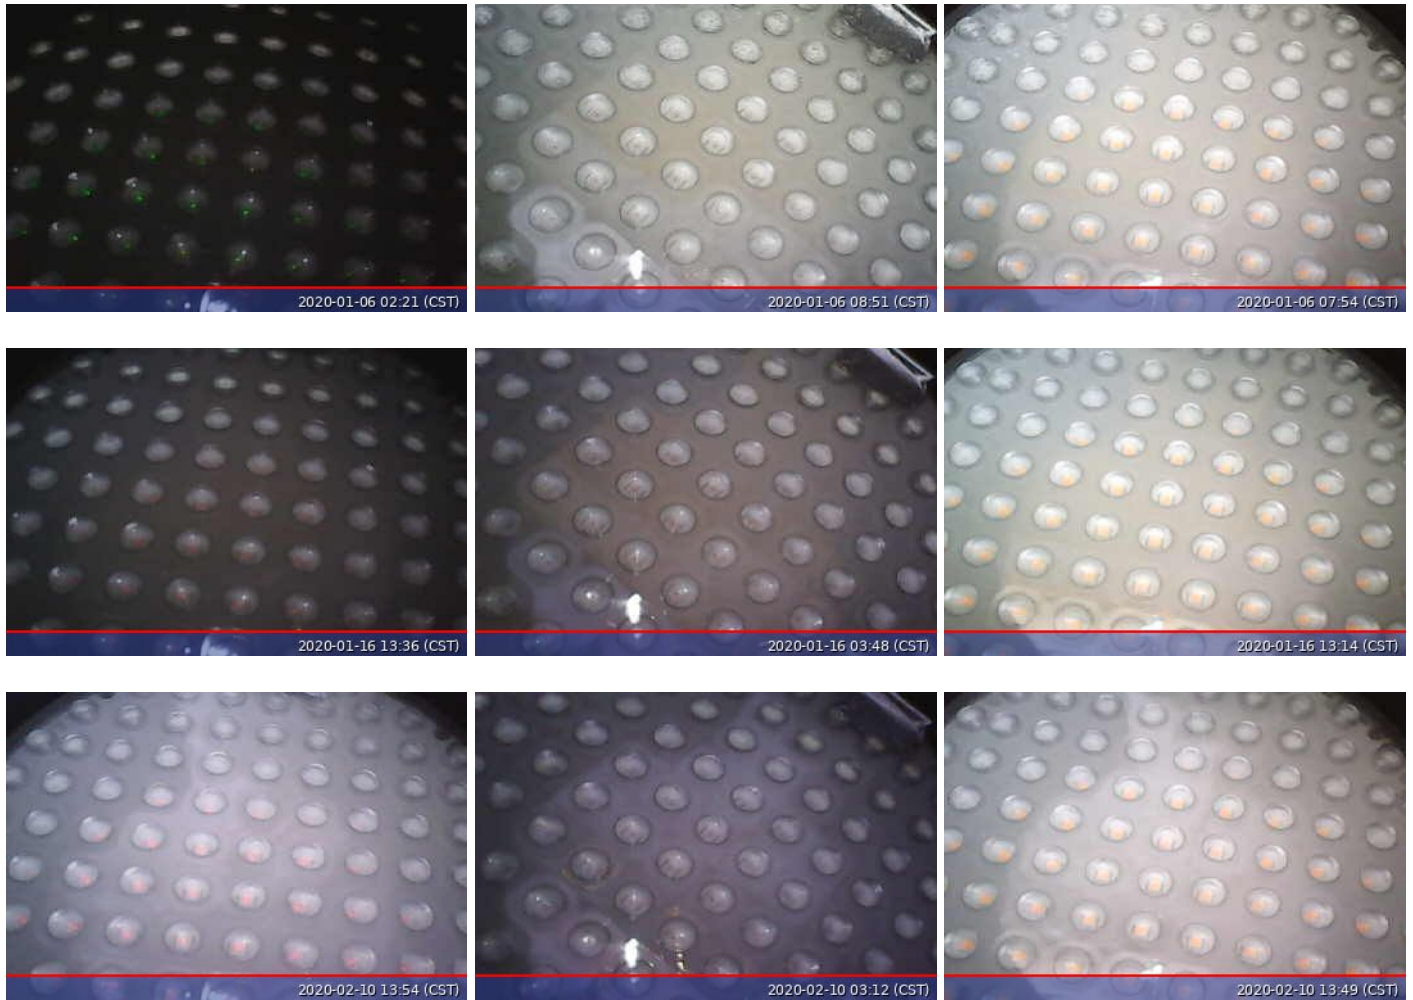

**Figure 5** Example pictures of the signals tested in Lawrence field site in the coldest days in winter 2020, automatically taken by the monitoring system.

Since the new remote monitoring system with mobile communication mounted in Lawrence test site had records of network disconnection with unknown reasons and stopped sending data back to the laboratory, we are planning to schedule another visit to the test site to diagnose the hardware and try to solve this problem.

Once we received samples of the new fresnel disc with 96 small fresnel lenses integrated on it, we will start to make the fifth generation of prototypes of the final product, in preparation for other test sites in Michigan, New Jersey, Wisconsin, Pennsylvania, and Maryland.

**Anticipated work next quarter:**

Starting from Jan 1, 2021 till March 31, 2021, we are planning to conduct the following tasks.

1. Once received samples of the new fresnel disc with 96 small fresnel lenses integrated on it, we will assemble the finalized 5<sup>th</sup> generation of prototypes for field tests in Michigan, New Jersey, Wisconsin, Pennsylvania, and Maryland.
2. Work with the fresnel lens company to further improve the new fresnel lens disc with 96 small fresnel lenses integrated on it, based on possible defectiveness or problems we might find.
3. Fix the problem of network disconnection of the new remote monitoring system with mobile communication mounted in Lawrence test site, we are planning to schedule another visit to the test site to diagnose the hardware and try to solve this problem.
4. Continue to work with Michigan, New Jersey, Wisconsin, Pennsylvania, and Maryland to find the other 4 field test sites and the detailed plan on field installations. Due to COVID-19, the actual field installation may be postponed.

**Significant Results:**

As of Dec 31, 2020, we have achieved the following significant results.

- This project was launched in Aug 2016 with six participating states (Kansas, California, Michigan, New Jersey, Wisconsin, and Pennsylvania) and an initial budget of \$240,000. Maryland is expected to officially join the study by the end of this year with additional contribution of three years funding.
- An expert panel meeting was held in early March. Discussions were held on desired specifications of the prototype signals and possible field test sites as well as the field evaluation of the prototypes.
- Necessary equipment, components and insulation materials are being procured to develop and build the fully working prototypes of the finalized design and test for their thermal and lighting performance. We will continue to order LED drivers, electricity monitors, waterproof security video cameras, other mounting accessories and materials, etc., for monitoring the performance of the prototypes in the field tests in the upcoming winter season.
- Appropriate color LED modules, which are not available in the market, were designed in-house and custom-made with the aid of the industrial partner.
- Three preliminary prototype signals (Red, Yellow, and Green) of Type 1 have been developed in house, each deploying 26 custom-made color LEDs mounted in an array via “Heat Arrangement of LED Arrays in Low Profile”. They are under laboratory testing for improvements.
- Tested the lighting and thermal performance of the preliminary prototypes of the Type 1 signal lights (Figure 1). Based on the test results, new design with a lot of changes and improvements has been finalized for final products.

- Finalized the design of Type 1 self de-icing LED signals using 96 custom-made mediate-power color LEDs mounted in an array via “Heat Arrangement of LED Arrays in Low Profile”. Designed in house and custom-made our own color LED modules (for each color R, G, Y) for making the fully working prototype signals of the first type with the aid of our industrial partner.
- Worked with the factories to optimize the mounting method of the custom-made LED modules on the 3-5 mm thick aluminum MPCB back plate serving as the passive heat exchangers of aluminum alloy for assembly.
- Custom-made three prototypes of the LED signals of Type 1 using 96 custom-made mediate-power color LEDs mounted in an array via “Heat Arrangement of LED Arrays in Low Profile”, with regular paint coating, and finished laboratory testing for improvements and optimizations to finalize the design.
- Improved and custom-made three new signal light engines using 96 medium-power LEDs (0.25 Watt each) mounted in an array via “Heat Arrangement of LED Arrays in Low Profile” but with Tin coating (Figure 3) and tested them to improve the heating performance (to make faster heat transfer).
- Finalized the design of the signal lens that adopts a whole piece design with smooth and flat outside surface and integrated with 96 additional custom-made Fresnel lenses sitting inside the signal lens over each LED on the inside surface to focus the light serving as a collimator lens. Based on the testing results, the signal light engines with TIN coating may have superior thermal performance, however, further testing in the laboratory and field is necessary to validate the final choice.
- Identified and started custom-making the Fresnel Lens from HongXuan Optoelectronic company with diameter 15 mm and focal length 6 mm (model # HX-F015006).
- Developed the new whole-piece signal housing, new Fresnel lenses, LED drivers, and other accessories for the Type 1 self de-icing LED signal lights, with the aid of the industrial partner.
- Found and selected a qualified plastic molding company to custom make the three parts of the plastic housing of fully working prototypes of Type 1 signals that deploy 96 mediate-power LEDs via the architecture of “Heat Arrangement of LED Arrays in Low Profile”. The new housing will be used for the new LED signal lights.
- The non-provisional patent application for the invention of Type 2 self de-icing signal light was officially approved by the USPTO and issued on Dec 26, 2017, patent No. US 9,851,086 B2.
- Started custom-making and modeling of the signal housing. Three samples were delivered for examinations and laboratory tests for necessary calibrations and further improvements.
- Started custom-making the LED drivers with desired specifications based on our test results. Seven LED drivers were delivered for sample testing.
- The custom-made signal housing is ready for production of products with possible minor adjustments for field tests in different states. Six improved samples have been delivered and thoroughly tested in laboratory and closed-setting tests on the roof.
- New type of screws for uses in the signal housing are self-designed and will be custom-made with



Fastenal company.

- A company is custom making two improved and finalized types of LED driver, one for YELLOW and GREEN signal lights (output 0.8 A, maximum 30 Watts), the other for RED signal light (output 1.1 A, maximum 30 Watts). The new LED drivers have temperature Sensor control, when the temperature is above 4 degree Celsius, the LED driver output will be derated (For Yellow + Green LED lights, output current 0.5 A, approximately 17- 18 Watts; For Red LED light, output current min 0.6 A, approximately 15-16 Watts.) When the temperature sensor is turned off or failed for any reasons, the power output will be restored to 100% as default.
- The self-deicing signal lights have higher light output than the codes and standards required in all viewing angles from 0 deg to 70 deg as measured, even at the derated power output.
- We have been conducting a closed-course performance and reliability tests of the fully working prototypes mounted on the roof of the University of Kansas engineering complex - M2SEC building, in preparation for field tests.
- Seven states have officially participated in this project, including Kansas, California, Michigan, New Jersey, Wisconsin, Pennsylvania and Maryland to provide support.
- A project addendum is proposed to conduct two additional field tests, one in Wisconsin and another one in a test site among Maryland, Pennsylvania, and New Jersey. A budget of \$80,000 for the addendum is proposed to be spent starting on 5/18/2018 until the end of the project
- We have been continuously testing the closed-course performance and reliability of the prototypes previously mounted on the roof of M2SEC building. All signal lights were powered by the signal controller cabinet with real signaling time cycles (in a cycle length of 90 seconds, Red signal light ON for 50 seconds, Green signal light ON for 35 seconds, and Yellow signal light ON for 5 seconds. The temperature data were recorded every 10 seconds continuously over the entire test period, which will be continuously conducted over both winter and summer seasons in 2019.
- We have designed and custom made new types of screws to improve the connection strength of the screws integrated with the plastic housing. This type of screws are finalized products to be used in all finalized plastic housing.
- We have designed and custom made two types of LED drivers, including one type of custom-made LED driver for **red signal light** (input: 100-240 VAC, output: 0.6-1.1 A, max 30 W), and a second type custom made LED driver for **green/yellow signal light** (input: 100-240 VAC, output: 0.5-0.8 A, max 30 W). Both types of LED drivers are now integrated with a remote temperature sensor for controlling the power output in light of the ambient air temperature. An on/off switch is designed for temperature controls in winter and summer modes which could override the operation of the temperature sensor.
- We have accordingly improved and finalized the plastic housing of the fully working prototype signals of Type 1 with changes/improvements listed below, with assist of the plastic molding company — Eco Molding. Eco Molding company has custom made seven samples of the finalized new plastic housing for validations tests before actual product production.
- We have produced 60 pcs of the finalized LED engines with the aid of the industrial partner, ready for

the upcoming field tests.

- We have also updated and custom made 60 pcs of glass disc which have four small mounting holes removed on the edge (the original glass disc had 8 mounting holes).
- We also custom made plastic mounting bars for mounting the glass disc to the LED light engine.
- We are working on getting improvement on custom-made Fresnel lens model number HX-F0150115 (diameter 15 mm, thickness 2.0 mm, focal length 11.5 mm) to increase tolerance of the thickness (approximately 1.8 – 2.1 mm) while reducing the unit cost.
- We are in preparation for field tests. Three fully functional prototypes of the fourth generation were mounted on a signal pole on the roof of an engineering building, powered by a traffic control cabinet for closed-course performance and reliability tests.
- Three more fully functional prototypes of the fourth generation were also tested in a well-controlled cold room for the performance of the ambient temperature sensor connected to the LED driver for switching full/derated power output. Based on the test results, we are adjusting the power output of the LED drivers. We are also making minor adjustments of the signal housing for quick assembly of the real products. Results have been used to evaluate the readiness of the prototypes for field tests starting in next quarter.
- Corrected some problems and resolved issues of the custom-made LED drivers, including (1) decreased the size of the power connector of the temperature sensor, (2) decreased the length to 6 mm, (3) changed to more reliable single switch, (4) enlarged the inside size of the installation hole to 6mm x 4.5 mm, (5) changed the final designed output current of Yellow/Green LED drivers to 0.40 A (derated) /0.84 A(full output), (6) changed the final designed output current of Red LED drivers to 0.60 A (derated) /1.1 A(full output), (7) improvements on temperature measurement accuracy, redesigned logic circuits, and changes of electronic parts used on the LED PCB boards.
- The signal housing of the fourth generation LED signal lights was revised for quick assembly. We have received the new prototypes of the housing with desired changes, which were tested in the laboratory with satisfactory performance.
- Other parts like glass mounting discs have also been improved in house for enlarging the installation holes to fit the new housing.
- Additional vendors for Fresnel lenses were contacted for lower unit price with higher quality control than the current lens vendor. Based on the lab test results, a total of 5000 PCS of new Fresnel lenses (**Model #1511**) were ordered from the new vendor for field tests.
- Based on the lab test results on the second generation of LED drivers, a total of 21 pcs of the third generation of LED drivers were ordered for lab tests, in preparation for the field tests.
- A total of 21 new LED drivers of the third generation for the field tests were made and are under testing in the laboratory for their field performance and any possible further improvements in need for control of the yield rate in production.
- A new proposal was approved on extended work with increased total project cost of \$360K and extended new end date of June 30, 2021.

- Field monitoring systems powered by Raspberry 3 B+ motherboard, fitted with three cable cameras used to monitor three signal lights (Red, Yellow, Green) in each unit, four temperature sensors used to record the lens' surface temperature of the three signal lights (Red, Yellow, Green) and the ambient air temperature, USB flash drivers used to store the year around test data (pictures and temperature dataset), power supplies, and mounting accessories, have been custom built in house and under testing in the lab and on the roof, which will be mounted at each field test site for year-around real-time monitoring and data recording of the new signals to be tested in the field.
- New fully working prototypes of the signal lights for field tests have been assembled and are under thorough final tests in the laboratory in preparation for upcoming field tests.
- A total of 21 new LED drivers of the third generation were tested for their field performance and further improvements needed for the control of the yield rate in production. Based on the test results, the third-generation LED drivers may need further improvements towards the fourth generation, which will resolve two issues: 1) light power-up delay (the time delay between power on and signal light on) for about 0.5-1 second, 2) Unstable output performance of the drivers, due to unsecured soldering of wire connections by hands.
- The field monitoring system consisting of a Raspberry PI computer, three cable cameras, four temperature sensors, USB flash drivers, power supplies, and mounting accessories, was built in-house and continuously tested in the laboratory and on the roof for field installation. The system will be mounted at every field test site for year-around real-time monitoring and data recording of the new signals.
- The first field test site was set up in Kansas at the intersection of County Rd 458 (or 1200 Rd) /US-59. All new equipment including the performance monitoring system for data recording were installed on side signals facing north and already survived the first snowstorm in December.
- More prototypes of the final products are in preparation for other test sites. Seven states (Kansas, California, Michigan, New Jersey, Wisconsin, Pennsylvania, and Maryland) are participating in field testing and evaluation of the prototypes.
- A remedying method in the laboratory for flattening the concaved lens surface, using supplemental heat beneath the lens and added weight on the top inside surface, a thermal lamp was installed inside a box below the glass on which the lens sits, the lens surface was monitored with four temperature sensors connected to a HOBO data logger.
- Talked with the fresnel lens company to modify the design and form factor of the currently adopted 96 individual lenses mounted in the housing to a whole piece of disc embedded with a total of 96 fresnel lenses on it.
- The field monitoring system has added mobile communication information device with data plan to remotely send the data of the signal performance back to the laboratory on daily basis for real-time performance monitoring, which is under testing on the roof.
- The problem of defective signal light housing with concave lens surface made during the production process has been solved with improved molding technology. A total of 100 new samples are made of Markrolon 2807 and tested with a maximum tolerance of 1.5 mm for mass production.

- A new fresnel disc with 96 small fresnel lenses integrated on it has been designed with the desired improvements, and is currently being custom-made in a factory through injection mold.
- We have installed the new remote monitoring system with mobile communication in the Lawrence test site, in addition to the original reliable “local” data monitoring system that kept running in the past year.
- The self-de-icing signals have survived both winter and summer functioning as expected, without any signs of snow and ice accumulation on the signal lens in cold winter, and abnormal performance in hot summer.

**Circumstance affecting project or budget. (Please describe any challenges encountered or anticipated that might affect the completion of the project within the time, scope and fiscal constraints set forth in the agreement, along with recommended solutions to those problems).**

None.
