


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	
1		RPMD Project	218 days	Wed 6/4/14	Mon 4/6/15		
2	✓	Project Kickoff Meeting	1 day	Wed 6/4/14	Wed 6/4/14		
3	✓	Note Sent To TAC	1 day	Thu 6/5/14	Thu 6/5/14	2	
4	✓	Note Sent to RAC	1 day	Thu 6/5/14	Thu 6/5/14	2	
5	✓	Send Emails to State DOT Research Leads	56 days	Thu 6/5/14	Fri 8/22/14		
6	✓	Created State Communication Tracking Spreadsheet	1 day	Thu 6/5/14	Thu 6/5/14		
7	✓	Prepare Folders for Responses	1 day	Fri 6/6/14	Fri 6/6/14		
8	✓	Create Email Template	1 day	Fri 6/6/14	Fri 6/6/14		
9	✓	Email Template Approval	1 day	Mon 6/9/14	Mon 6/9/14	8	
10	✓	Send Emails to Receptients	4 days	Mon 6/9/14	Thu 6/12/14		
11	✓	Follow Up with Non-Responders/Responders	40 days	Fri 6/13/14	Thu 8/7/14	10	
12	✓	Organize Responses	10 days	Fri 8/8/14	Thu 8/21/14	11	
13	✓	Ready to begin investigating tools!	0 days	Fri 8/22/14	Fri 8/22/14	12	
14		Compare State Databases and Spreadsheets	78 days	Fri 8/22/14	Tue 12/9/14		
15		Research comparison tools	60 days	Fri 8/22/14	Thu 11/13/14	13	
16		Test comparison tools	18 days	Fri 11/14/14	Tue 12/9/14	15	
17		Decide on best comparison tool	0 days	Tue 12/9/14	Tue 12/9/14	16	
18		Organize Information Received	120 days	Fri 8/22/14	Thu 2/5/15		
19		Prepare data for comparing data	60 days	Fri 8/22/14	Thu 11/13/14	13	
20		Compare data	60 days	Fri 11/14/14	Thu 2/5/15	19	
21		Schemas compared!	0 days	Thu 2/5/15	Thu 2/5/15	20	
22		Create Best Practices Presentation	41 days	Fri 2/6/15	Mon 4/6/15		
23		Identify requirements for presentation	30 days	Fri 2/6/15	Thu 3/19/15	21	
24		Draft presentation	11 days	Fri 3/20/15	Fri 4/3/15	23	
25		Report the presentation to the TAC	0 days	Mon 4/6/15	Mon 4/6/15	24	

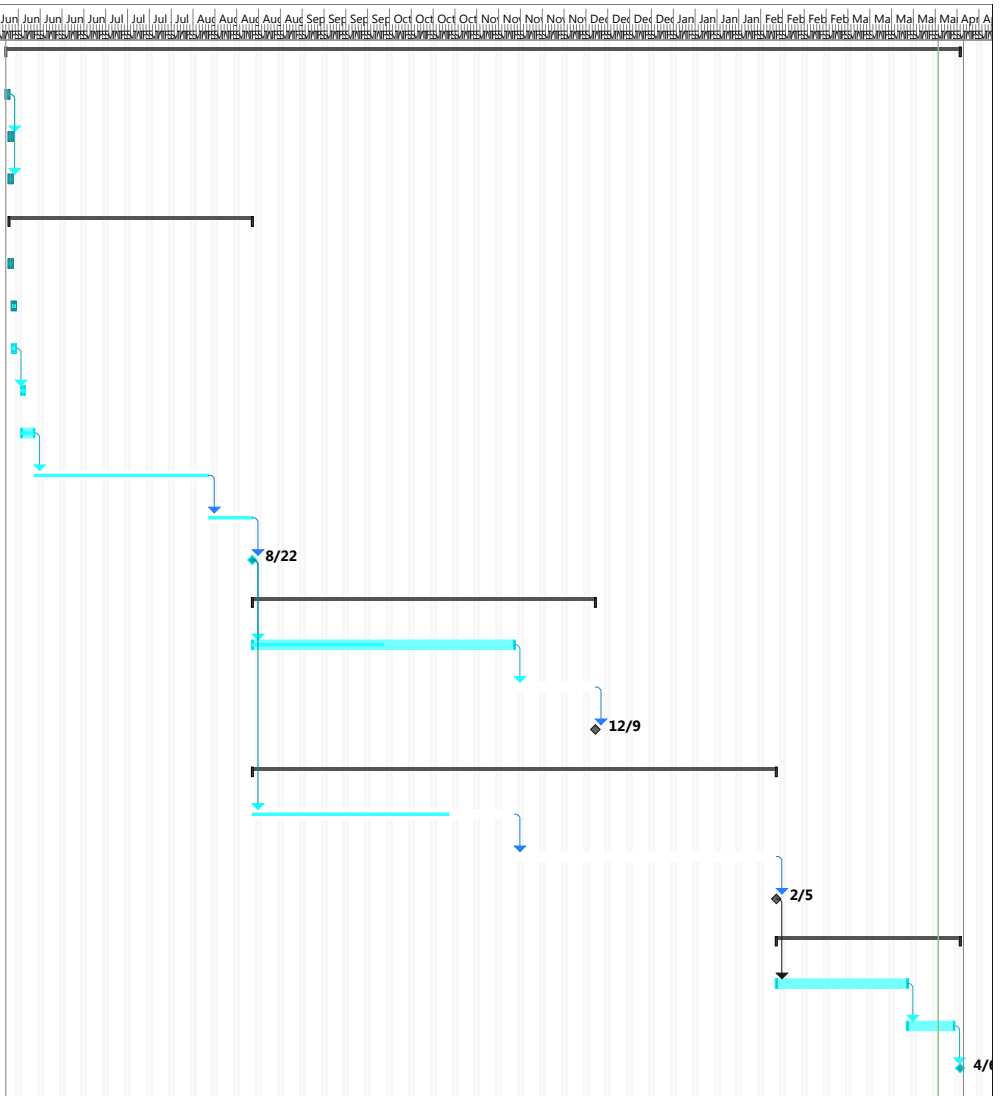

Project: RPMD Project.mpp

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
